Zoning Ordinance Rewrite (Work Plan)

PC Dicsussion ✦ BOS/PC Disc. ✦ **Current Status:** 16 — Plan Duration | Actual Start | % Complete | Actual (beyond plan) | % Complete (beyond plan)

ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLETE
PHASE I					
Definitions (Completed)	1	1	1	1	100%
Use Table (Completed)	1	1	1	1	100%
Districts (C-2, SC-1, SF-1, B-1, B-4, I-1, RC-1, RC-2, C-1, Completed)	1	1	1	1	100%
Districts (RMX/B-2)	1	2	1	2	100%
District Reviews (MF-1 & MH-1)	2	2	2	2	100%
District Reviews (Residential / Conservation / Agricultural Districts)	3	2	3	2	100%
Joint Meeting w/ Board of Supervisors (2nd Tuesday of the month)					100%
District Reviews (Business/Industrial District)	4	2	4	2	100%
Subdivision Ordinance - BLA Code Amendment and Identification of Revisions Based on District Reviews Only	3	6	3	9	75%
Supplemental District Regulations (General Plan of Action)	7	2	6	4	100%
Supplemental District Regulations (Residential/Civic/Ag)	8	3	8	8	100%
Supplemental District Regulations (CP&S, Industrial, Utilities/Tele)	10	3	15		50%
Supplemental Regulations (General Development Regulations)	12	3			0%
General Citizen Input / Beehive Articles	4	22	4	12	50%
Focus Group Input	20	6			0%
Article 11 & 12 - Parking and Signs (just to update for uses/district names)	14	3			0%
Article 14 - Administrative Procedures (simplify, update, SE criteria)	16	3			0%
Article 15 - Enforcement (coordination between Planning/Building/Environmental	18	3			0%
Final Revisions / Discussions (Articles 1, 3, & 13)	20	3			0%

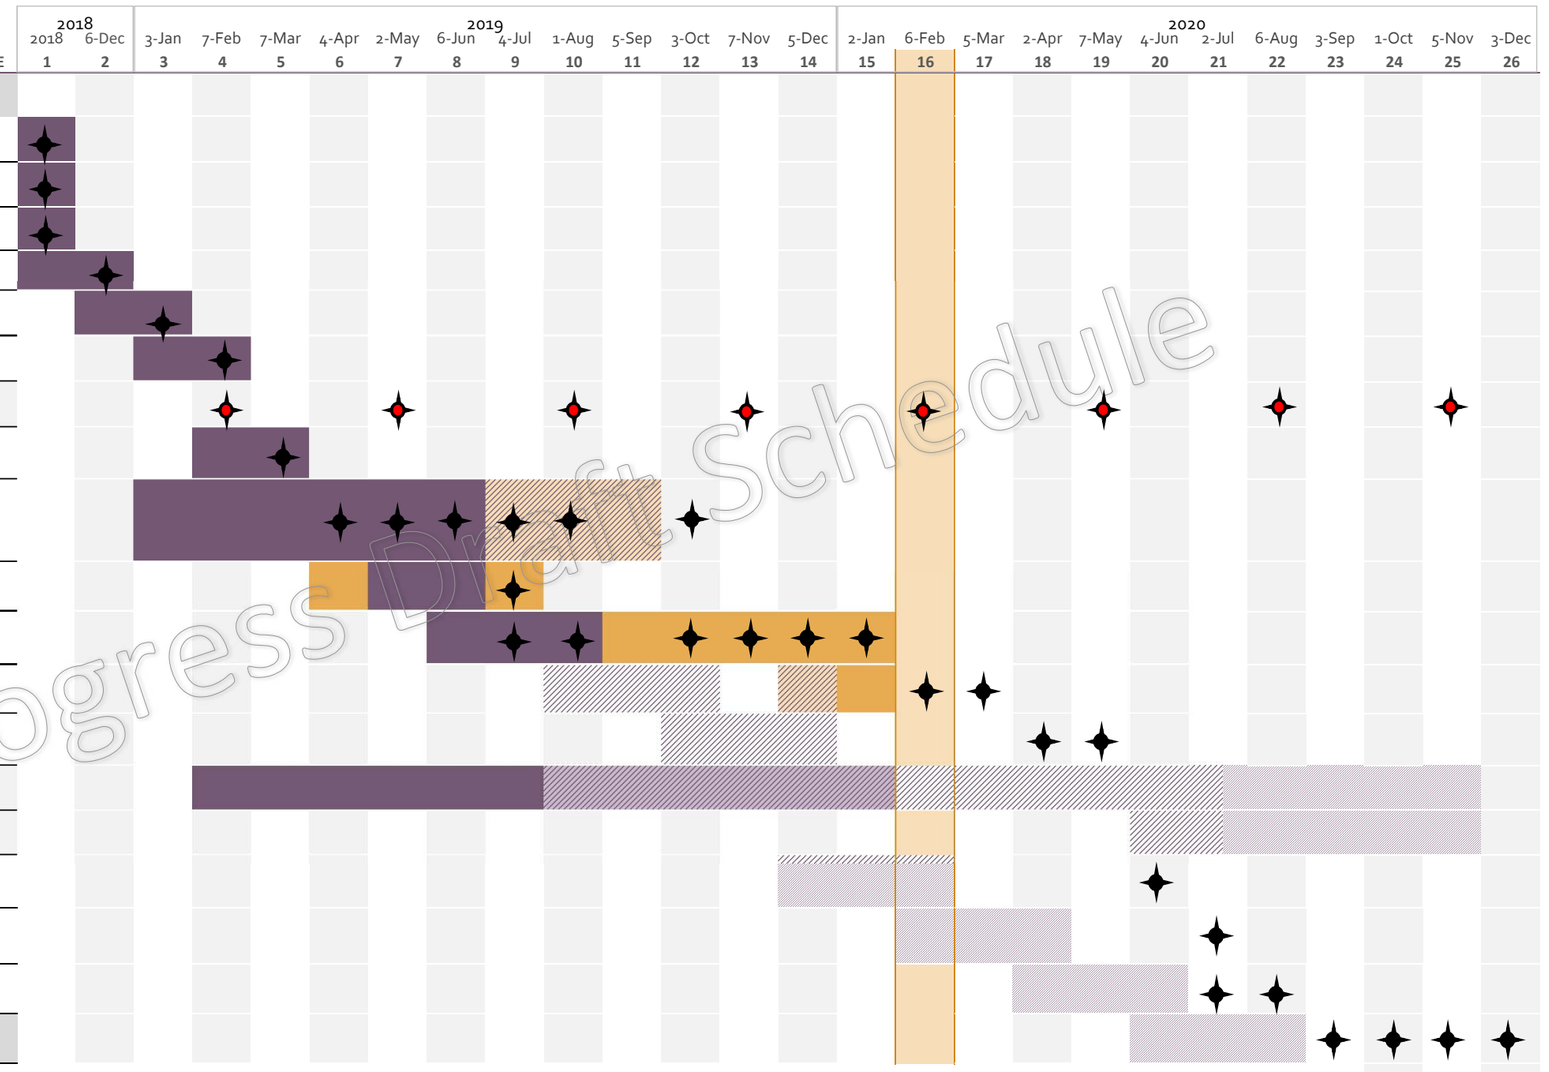

In-Progress Draft Schedule

Note: The schedule presented identifies staff targets. These targets are subject to change based on priorities shifting and the Planning Commission's and Board's input and expectations during discussion of revisions. Updated 2/3/2020
